FDOT Contract T5404

SR 40 Ormand Beach Contract ID: T5467

Project ID: T5467-00

Data Date: 3.1.14 / Run Date: 2.25.14

HALIFAX PAVING INC.

Activity ID	Activity Name	Org Dur	Rem Dur	Start	Finish	Actual Start	Actual Finish	Early Start	Late Start	Total Float
SR 40 Ormand Beach Contract ID: T5467		264d	264d	3.1.14	11.19.14			3.1.14	3.1.14	0d
1000	NTP	0d	0d	3.1.14				3.1.14	3.1.14	0d
1010	Mobilization	7d	7d	3.1.14	3.7.14			3.1.14	3.1.14	0d
PHASE 1 STA 1343+25 TO 1593+67 OUTSIDE LANES		97d	97d	3.8.14	6.12.14			3.8.14	3.8.14	160d
1100	INSTALL LEAD-IN SIGNS BARRICADES	10d	10d	3.8.14	3.17.14			3.8.14	3.8.14	0d
1200	INSTALL EROSION PROTECTION	5d	5d	3.18.14	3.22.14			3.18.14	3.18.14	0d
1250	UTILITY ADJUSTMENTS MANHOLES VALVES RING & COVER	14d	14d	3.18.14	3.31.14			3.18.14	10.23.14	219d
1251	UTILITY ADJUSTMENTS MANHOLES VALVES RING & COVER	14d	14d	4.1.14	4.14.14			4.1.14	11.6.14	219d
1252	UTILITY ADJUSTMENTS MANHOLES VALVES RING & COVER	14d	14d	3.18.14	3.31.14			3.18.14	10.23.14	219d
1253	UTILITY ADJUSTMENTS MANHOLES VALVES RING & COVER	14d	14d	4.1.14	4.14.14			4.1.14	11.6.14	219d
1300	CLEAR & GRUBB EARTHWORK EB OUTSIDE SHOULDERS	14d	14d	3.18.14	3.31.14			3.18.14	3.18.14	0d
1350	CONSTRUCT SIDEWALKS ADA IMPROVEMENTS EASTBOUNI	21d	21d	3.18.14	4.7.14			3.18.14	10.30.14	226d
1370	INSTALL TEMPORARY TRAFFIC DETECTION	5d	5d	3.18.14	3.22.14			3.18.14	11.15.14	242d
1400	INSTALL STORM DRAINAGE	21d	21d	3.18.14	4.7.14			3.18.14	4.1.14	14d
1500	INSTALL TRAFFIC SIGNAL CONDUIT MAST ARMS	30d	30d	4.1.14	4.30.14			4.1.14	10.21.14	203d
1550	INSTALL ASPHALT WIDENING, SHOULDERS	11d	11d	4.1.14	4.11.14			4.1.14	4.1.14	0d
1600	MILL AND RESURFACE EASTBOUND OUTSIDE LANE TURN L	10d	10d	4.12.14	4.21.14			4.12.14	4.12.14	0d
1650	INSTALL TEMP PAVEMENT MARKINGS	4d	4d	4.22.14	4.25.14			4.22.14	4.22.14	0d
1670	SOD SHOULDERS EASTBOUND	10d	10d	4.26.14	5.5.14			4.26.14	4.26.14	0d
1700	CLEAR & GRUBB EARTHWORK WB OUTSIDE SHOULDERS	14d	14d	5.6.14	5.19.14			5.6.14	5.6.14	0d
1750	CONSTRUCT SIDEWALKS ADA IMPROVEMENTS WESTBOUN	30d	30d	5.6.14	6.4.14			5.6.14	10.21.14	168d
1800	INSTALL STORM DRAINAGE WESTBOUND	7d	7d	5.6.14	5.12.14			5.6.14	5.6.14	0d
1850	INSTALL TRAFFIC SIGNAL CONDUIT MAST ARMS	30d	30d	5.6.14	6.4.14			5.6.14	6.28.14	53d
1900	INSTALL ASPHALT WIDENING, SHOULDERS	14d	14d	5.6.14	5.19.14			5.6.14	5.6.14	0d
1950	MILL AND RESURFACE WESTBOUND OUTSIDE LANE TURN L	10d	10d	5.20.14	5.29.14			5.20.14	5.20.14	0d
1951	INSTALL TEMP PAVEMENT MARKINGS	4d	4d	5.30.14	6.2.14			5.30.14	5.30.14	0d
1952	SOD SHOULDERS	10d	10d	6.3.14	6.12.14			6.3.14	6.3.14	0d
PHASE 2 STA 1343+25 TO 1593+67 INSIDE LANES		154d	154d	5.6.14	10.6.14			5.6.14	6.13.14	44d
2000	CLEAR & GRUBB EARTHWORK EB INSIDE SHOULDERS	16d	16d	6.13.14	6.28.14			6.13.14	6.13.14	0d
2050	CONSTRUCT SIDEWALKS ADA IMPROVEMENTS EASTBOUNI	30d	30d	6.13.14	7.12.14			6.13.14	10.21.14	130d
2100	INSTALL TEMPORARY TRAFFIC DETECTION	4d	4d	6.13.14	6.16.14			6.13.14	11.16.14	156d
2150	INSTALL STORM DRAINAGE	7d	7d	6.13.14	6.19.14			6.13.14	11.13.14	153d
2200	INSTALL TRAFFIC SIGNAL CONDUIT MAST ARMS	30d	30d	5.6.14	6.4.14			5.6.14	6.28.14	53d
2250	INSTALL ASPHALT WIDENING, SHOULDERS	14d	14d	6.29.14	7.12.14			6.29.14	6.29.14	0d
2300	MILL AND RESURFACE EASTBOUND INSIDE LANE TURN LAN	10d	10d	7.13.14	7.22.14			7.13.14	7.13.14	0d
2350	INSTALL TEMP PAVEMENT MARKINGS	4d	4d	7.23.14	7.26.14			7.23.14	7.23.14	0d
2400	SOD SHOULDERS EASTBOUND	10d	10d	7.27.14	8.5.14			7.27.14	7.27.14	0d
2450	CLEAR & GRUBB EARTHWORK WB INSIDE SHOULDERS	21d	21d	8.6.14	8.26.14			8.6.14	8.6.14	0d
2500	CONSTRUCT SIDEWALKS ADA IMPROVEMENTS WESTBOUN	30d	30d	8.6.14	9.4.14			8.6.14	10.21.14	76d
2550	INSTALL STORM DRAINAGE WESTBOUND	7d	7d	8.6.14	8.12.14			8.6.14	11.13.14	99d
2600	INSTALL TRAFFIC SIGNAL CONDUIT MAST ARMS	30d	30d	6.5.14	7.4.14			6.5.14	7.28.14	53d
2650	INSTALL ASPHALT WIDENING, SHOULDERS	7d	7d	8.27.14	9.2.14			8.27.14	8.27.14	0d
2700	MILL AND RESURFACE WESTBOUND INSIDE LANE TURN LAI	10d	10d	9.3.14	9.12.14			9.3.14	9.3.14	0d
2750	INSTALL TEMP PAVT MARKINGS & PERM SIGNS	14d	14d	9.13.14	9.26.14			9.13.14	10.27.14	44d
2800	SOD SHOULDERS	10d	10d	9.27.14	10.6.14			9.27.14	11.10.14	44d
2850	INSTALL TRAFFIC SIGNAL CONDUIT MAST ARMS	21d	21d	9.13.14	10.3.14			9.13.14	9.13.14	0d
2900	INSTALL TRAFFIC SIGNAL LOOPS	21d	21d	9.13.14	10.3.14			9.13.14	9.13.14	0d
PHASE 3 STA 1343+25 TO 1593+67 INSIDE LANES		47d	47d	10.4.14	11.19.14			10.4.14	10.4.14	0d
3000	INSTALL FINAL FRICTION COURSE EB OUTSIDE LANE	7d	7d	10.4.14	10.10.14			10.4.14	10.4.14	0d
3050	INSTALL FINAL FRICTION COURSE WB OUTSIDE LANE	7d	7d	10.11.14	10.17.14			10.11.14	10.11.14	0d
3100	INSTALL FINAL FRICTION COURSE EB INSDE LANE	7d	7d	10.18.14	10.24.14			10.18.14	10.18.14	0d
3150	INSTALL FINAL FRICTION COURSE WB INSIDE LANES	7d	7d	10.25.14	10.31.14			10.25.14	10.25.14	0d
3200	INSTALL FINAL TRAFFIC LOOPS	5d	5d	11.1.14	11.5.14			11.1.14	11.1.14	0d
3250	INSTALL FINAL PAVEMENT MARKINGS	14d	14d	11.6.14	11.19.14			11.6.14	11.6.14	0d

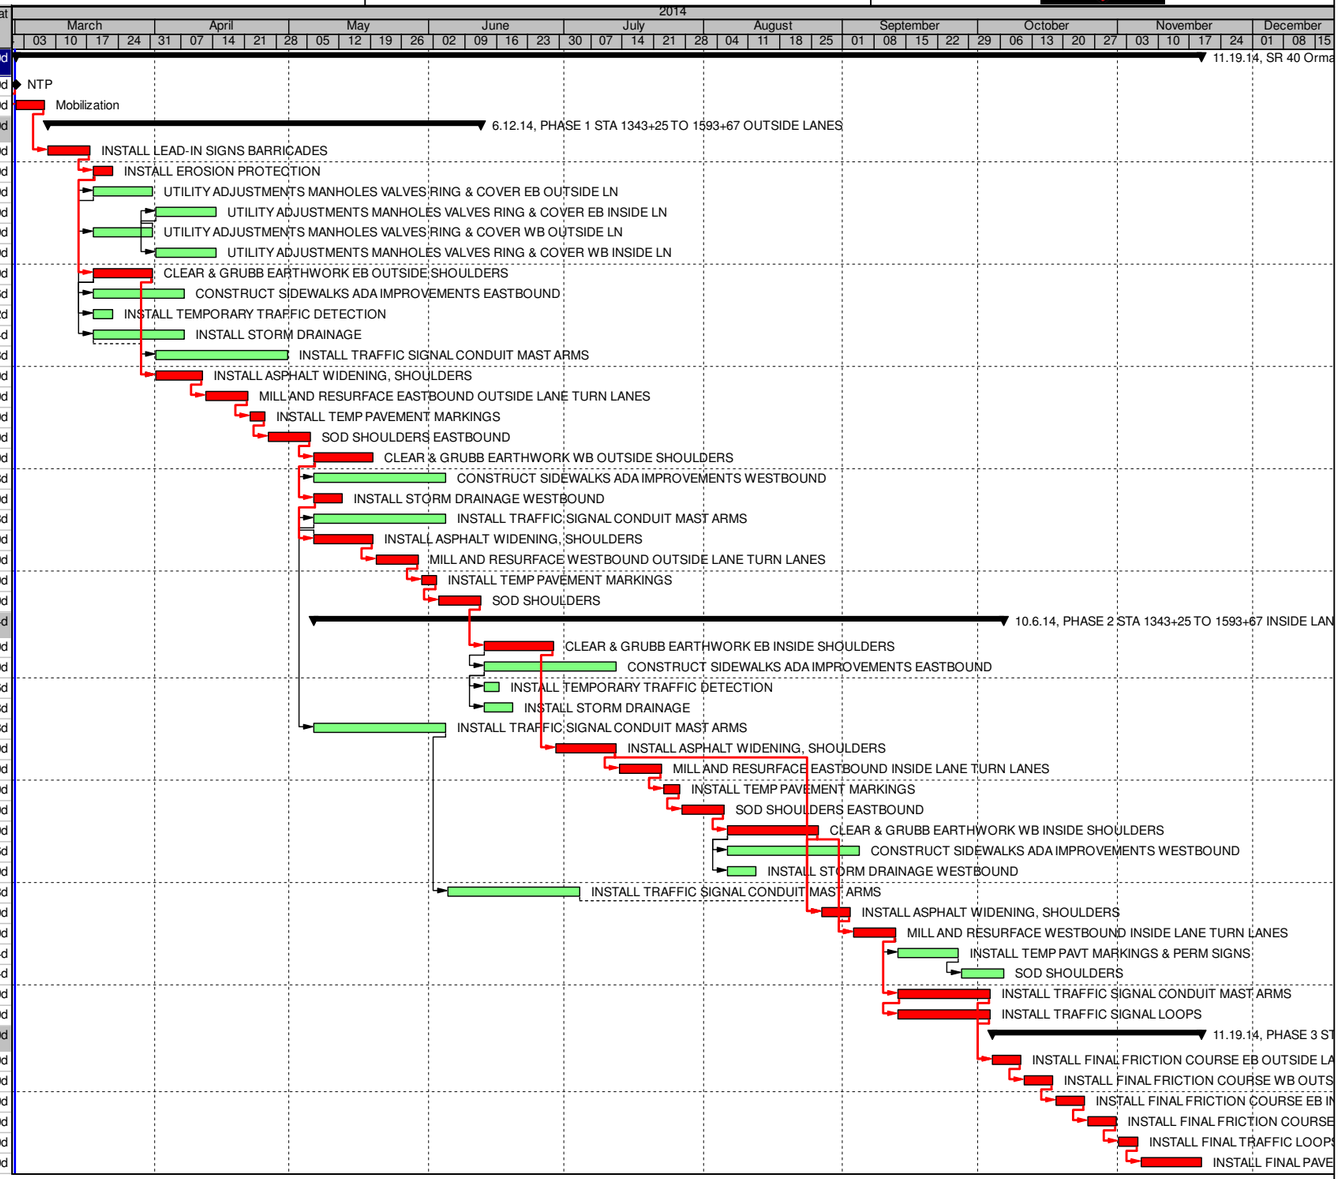

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary
WBS Summary Act...
WBS Summary Pr...

TASK filters: In Progress, Not Started.

Layout: 2014027 - T5467-Layout OPS

BASELINE CONSULTANTS, INC.
